


Foraje geotehnice/ Geotechnical borhole
Pod pe DX peste Canal la km 61+650/
Bridge on DX over Channel at km 61+650

Foraj nr: F5964
 km 90+260
 Scara 1:100

Adancime m	20.0	18.0	16.0	14.0	12.0	10.0	8.0	6.0	4.0	2.0
Descrierea Litologica	Soi vegetal	Argila prafoasa, cenusiu-cafenie cu concretioni calcaroase	Argila prafoasa, cenusiu-cafenie, cu concretioni calcaroase	Argila prafoasa, cenusiu-galbuie, consistenta	Nisip argilos, galbui-cenusiu, mediu indosat	Argila prafoasa, slab nisipoasa, cenusie-galbuie, consistenta/vartoasa				
Coloana stratigrafica	///	///	///	///	///	///	///	///	///	///
Adancime (m)	0.20	1.10	2.20	3.70	5.50	6.00				
Grosime (m)	0.20	0.90	1.00	1.50	1.80	0.50				
% Recuperare		100	100	100	100	100				
% RQD										
Probe Netuburate m										
Probe Tuburate m										
Adancime SPT m										
Piezometru si nivelul Apel m										
Coloana de Tubaj m										

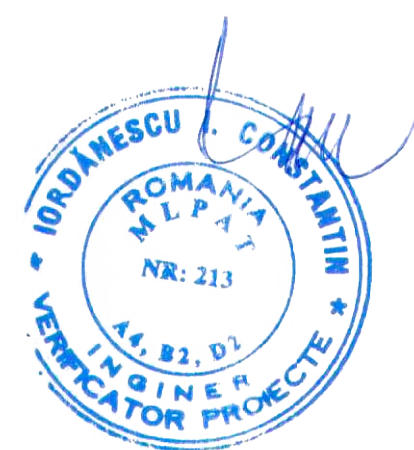

Pag. 1/1
 Intocmit: Lacatus Gheorghe
 Verificat: Ing. Marius Mantulescu
 Scara 1:100

PROIECTANT / DESIGNER: S.C. CONSITRANS S.R.L.	BENEFICIAR / BENEFICIARY: MUNICIPIUL ARAD, MUNICIPIUL ORADEA, CONSILIUL JUDETEAN ARAD, CONSILIUL JUDETEAN BIHOR CNAIR	FUNCTIA / POSITION: COORDONATOR DE PROIECT / PROJECT MANAGER	NUME / NAME: ing. S. VEACESLAV	SEMNTATURA / SIGNATURE: 	Titlu plansa / Drawing title: Foraje geotehnice/ Geotechnical Borhole Pod pe DX peste Canal la km 61+650 Bridge on DX over Channel at km 61+650	REV/ REV.: R00	DATA/ DATE: 11.2023	DETALII REVIZIE / REVISION DETAILS: P.T.E.	PROIECTAT / DESIGNER: Consitrans
INVESTITIA / INVESTMENT: ACTUALIZARE/COMPLETARE/REVIZUIRE (S.F. + P.A.C. + P.O.E + P.T.E.) "DRUM EXPRES ARAD ORADEA" ACTUALIZATION/COMPLETION (S.F. + P.A.C. + P.O.E + P.T.E.) "EXPRESS ROAD ARAD ORADEA"		SEF PROIECT SPECIALITATE / TEAM LEADER: ing. D. COVELTIR		ing. V. URDAREANU	LUCRARI DE POD / BRIDGE WORKS				
FAZA PROIECTARE / DESIGN STAGE: PROIECT TEHNIC DE EXECUTIE / EXECUTION TECHNICAL PROJECT		PROIECTAT / DESIGNER: ing. D. COVELTIR		ing. D. COVELTIR	Cod plansa / Drawing code: CST-0121-PTE-0-DX-02-P38-DGF-01-R00				
Contract /Contract: 14724/01.07.2021 Data / Date: 11.2023 Scara /Scale: 1:200		VERIFICAT / INTERNAL CHECKER:							

